

24 March 2021

18045-BOW Bowmar Elementary / Report Number 028

201 Park Court, Suite B Ridgeland, MS 39157 P 601.790.9432 F 888.281.0547	Contract	Paul Jackson & Son
	Date / Time	23 March 2021 / 12:30 PM
	Weather / Temp	Cloudy / 62 ° F
	Est % Complete	70%
One Jackson Place, Suite 250 188 East Capitol Street Jackson, MS 39201-2100 P 601.352.5411 F 601.352.5362	Sched Conformance	+/- 00 days
	Work in Progress	Mechanical Installers Electrical Installers Drywall Finishing
	Present at Site	Jimmy White, PJS Paul Purser, DBA
161 Lameuse Street, Suite 201 Biloxi, MS 39530 P 228.374.1409 F 228.374.1414	Observations	<p>On site, I met Jimmy White, Paul Jackson &amp; Son, at the rear addition. I reviewed the stucco work performed in a ten-foot section with him. The finish looks good, clean, and without defects.</p> <p>Finish work was also in progress at the interior. Drywall finishers were at work in several areas there. Also, mechanical and electrical workers were busy installing their corresponding trade items.</p> <p>A bracing style has been suggested by the contractor, noted in figure 5. This suggestion is being made due to conflicts between ducting and other above ceiling items and new bracing that was agreed upon 2 weeks ago. Mr. White says that they are unable to get a diagonal stud every 4' due to the conflicts so they are suggesting going all the way across, from wall to wall with a supporting stud.</p>
	Items to Verify	Acceptability of new stud arrangement in accordance with design intentions.
	Action Required	None
	Report By:	

Paul Purser, AIA, LEED AP  
Dale | Bailey, an Association

cc: James Brock / Jimmy White (PJS)  
Chad Shealy / Bill Sanderford (VWSD)  
Gary Bailey / Jason Stewart / Mark Pipper (BPM)  
Russ Blount / Travis Altsman / Abigail Raper / Candy Failor (DBA)  
Tom Schaeffer / Will Grigg (M)  
Kevin Starks / Jason Kackley / Al Guynes (GSK)  
Chris Green / Larry Scott (TPS)



Figure 1 – Finished Stucco Mockup Section



Figure 2 – Finished Stucco Mockup Section



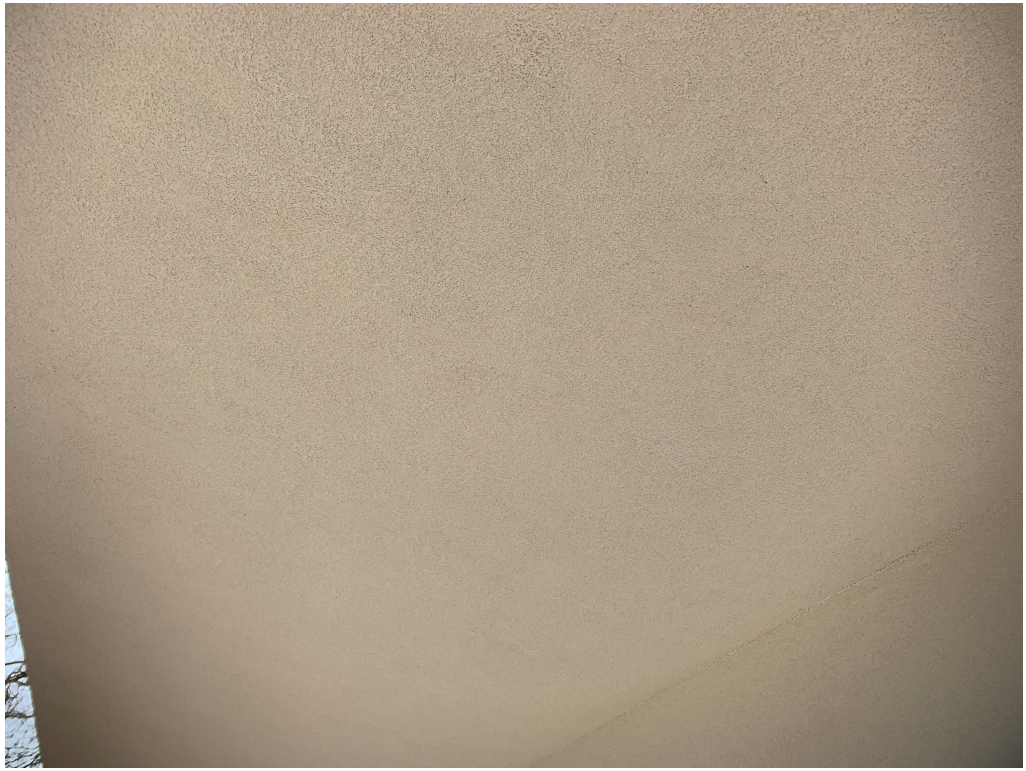


Figure 3 – Finished Stucco Mockup Section

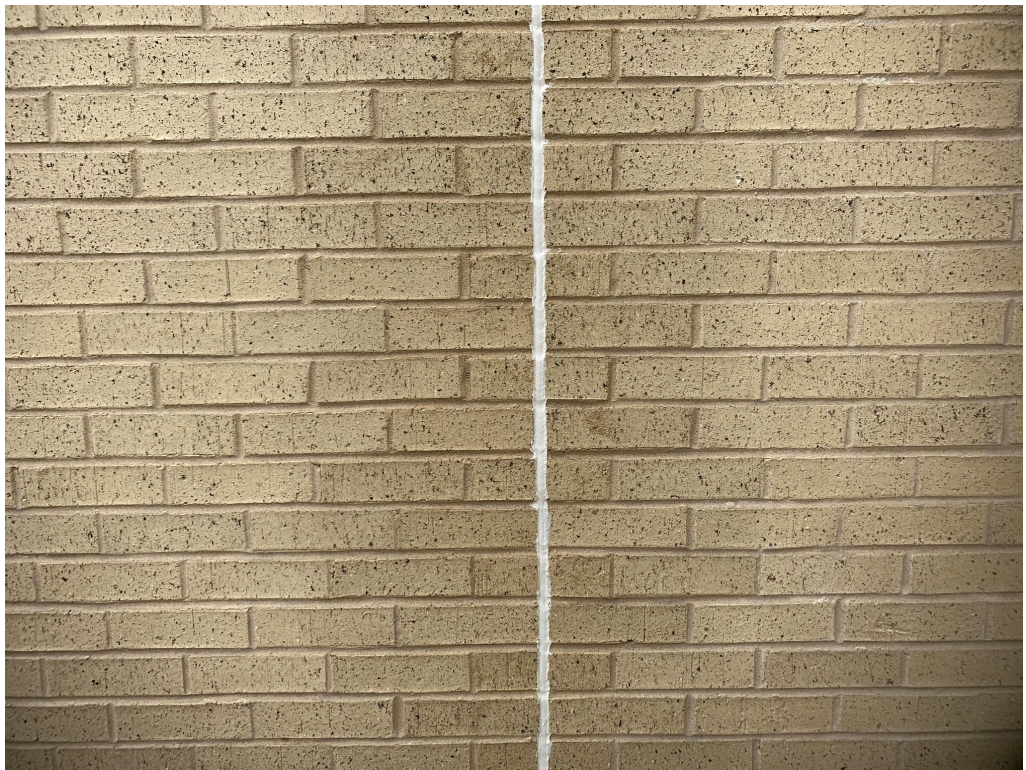


Figure 4 – Sealant Installed





Figure 5 – Bracing Suggested by Contractor



Figure 6 – Finish Work is Ongoing
