

## Architect's Field Report

201 Park Court, Suite B  
Ridgeland, MS 39157  
P 601.790.9432  
F 888.281.0547

01 July 2021

18053-Vicksburg Junior High School / Report Number 036

One Jackson Place, Suite 250  
188 East Capitol Street  
Jackson, MS 39201-2100  
P 601.352.5411  
F 601.352.5362

Contract Paul Jackson &amp; Son

Date / Time 30 June 2021 / 12:30 PM

Weather / Temp Partly cloudy / 91 ° F

Est % Complete 85%

Sched Conformance + 30 days

Work in Progress Metal Rail Installation, Mechanical Work, VCT Installation

Present at Site Jeff Porter, PJS  
Paul Purser, DBA

161 Lameuse Street, Suite 201  
Biloxi, MS 39530  
P 228.374.1409  
F 228.374.1414

Observations Arriving on site, I entered through the front entry. At the interior, floor prep has been performed and installation was ongoing for VCT flooring. Metal railing have been set in place where to be installed and are being checked for correct fitting before final installation per Jeff Porter (PJS).

I met him, Jeff Porter, at the exterior, and we discussed remaining tasks. We projected work to be nearing completion within 4 weeks. The addition should be complete soon, however, some above ceiling tasks remain per city requirements. The elevator is in working order but still needs to be switched from remote controls to wired. Some metal railings require rework but should be installed within the next couple of weeks. Asphalt overlay at the parking area is awaiting curb work as well.

Items to Verify None

Action Required None

Report By:



Paul Purser, AIA, LEED AP  
Dale | Bailey, an Association

cc: Austin Stults / Jeff Porter / Kipp Ready (PJS)  
Chad Shealy / Shaquita Burke / Christi Kilroy (VWSD)  
Gary Bailey / Jason Stewart / Mark Pipper (BPM)  
Russ Blount / Candy Failor (DBA)  
Brandon McKay / Austin Newell (WGK)  
Jason Kackley / Al Guynes (GSK)  
Chris Green / Larry Scott (TPS)  
Tom Schaeffer / Tad Hoffpaur (SDG)

dalepartners.com

baileyarch.com

Architects Who Know Education



Figure 1 – Front Façade



Figure 2 – Asphalt from Roof Work on Brick & Flashing



Figure 3 – Asphalt from Roof Work on Brick



Figure 4 – Concrete Splatter to be Removed



Figure 5 – Floor Prep at Addition

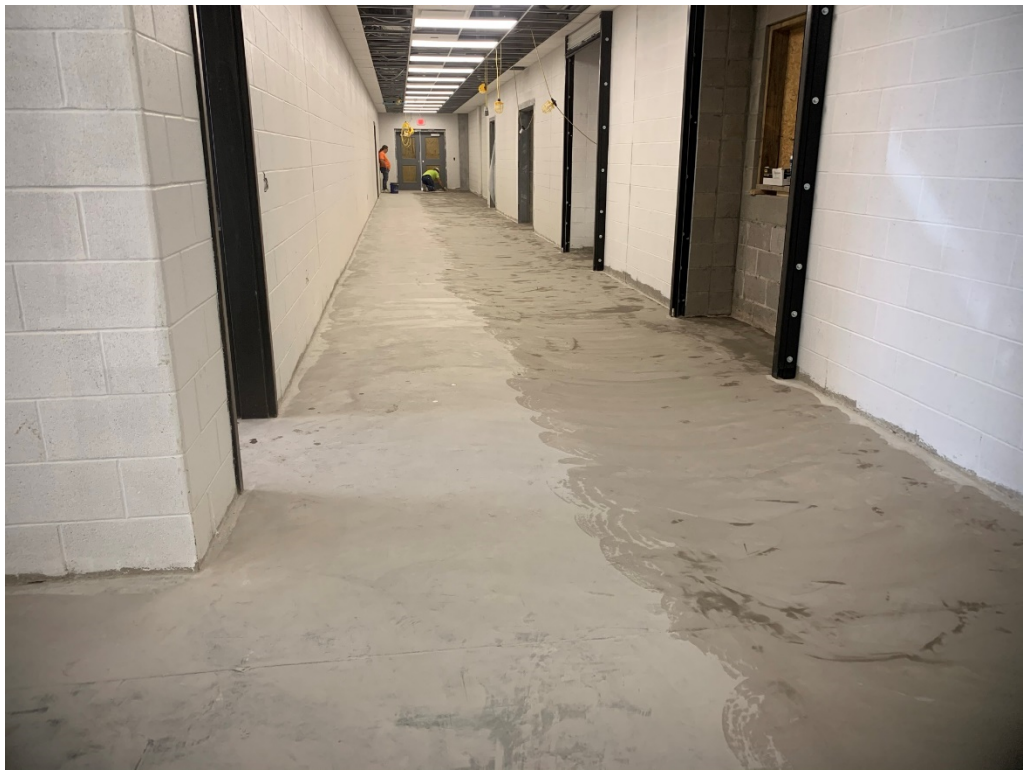


Figure 6 – Floor Prep at Addition



Figure 7 – VCT in Concessions Area



Figure 8 – Flooring Levelled Up and Ready for VCT

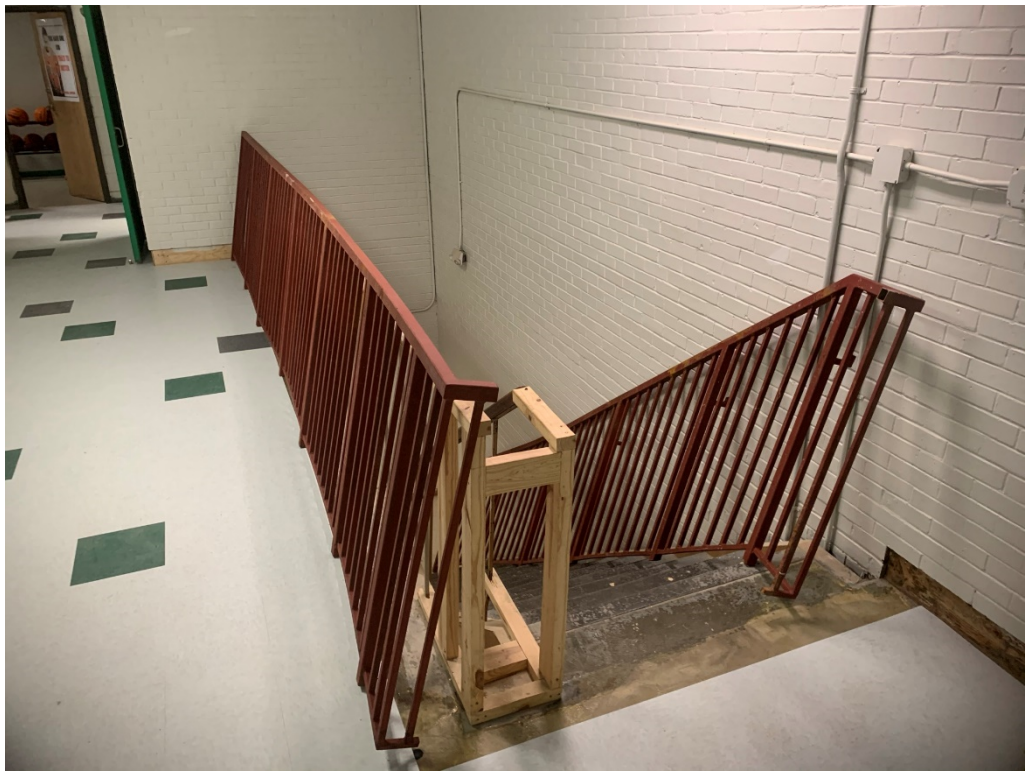


Figure 9 – Metal Railing being fitted



Figure 10 – Ceiling Tile awaiting Installation



Figure 11 – Metal Railing being fitted



Figure 12 – Jambs Still to be Finished at Bathrooms



Figure 13 – Jambs Still to be Finished at Bathrooms



Figure 14 – Masonry Work at Low Fence





Figure 15 – Masonry Work at Low Fence



Figure 16 – Filled Block Wall
