

Architect's Field Report

201 Park Court, Suite B
Ridgeland, MS 39157
P 601.790.9432
F 888.281.0547

03 March 2020

18056-Warren Central Junior High School / Report Number 001

One Jackson Place, Suite 250
188 East Capitol Street
Jackson, MS 39201-2100
P 601.352.5411
F 601.352.5362

Contract Paul Jackson & Son
Date / Time 02 March 2020 / 4:00 PM
Weather / Temp Cloudy / 70 ° F
Est % Complete 2%
Sched Conformance + 00 days
Work in Progress Ceiling Demo

161 Lameuse Street, Suite 201
Biloxi, MS 39530
P 228.374.1409
F 228.374.1414

Present at Site Tommy Stewart (PJS)
Paul Purser, DBA

Observations Arriving on site, I met Tommy Stewart outside waiting for student dismissal. We walked in together and reviewed work completed so far.

Ceiling Tile removal is ongoing and the majority of what has been complete. Mr. Stewart indicated also that Mr. Tim Wilson, superintendent was absent this week due to OSHA Exams.

There is one room that needs clearing by School Staff, room E-102C. It is a storage room on the first floor that has so much in it, it is preventing PJS Crew from performing their work.

Items to Verify None

Action Required None

Report By:

Paul Purser, AIA, LEED AP, Partner
Dale | Bailey, an Association

cc: Austin Stults / Tim Wilson / Chasity Cupstid (PJS)
Chad Shealy / Shaquita Burke / Christi Kilroy (VWSD)
Gary Bailey / Jason Stewart / Mark Pipper (BPM)
Russ Blount / Candy Failor (DBA)
Brandon McKay / Austin Newell (WGK)
Jason Kackley / Al Guynes (GSK)
Chris Green / Larry Scott (TPS)
Tom Schaeffer (SDG)

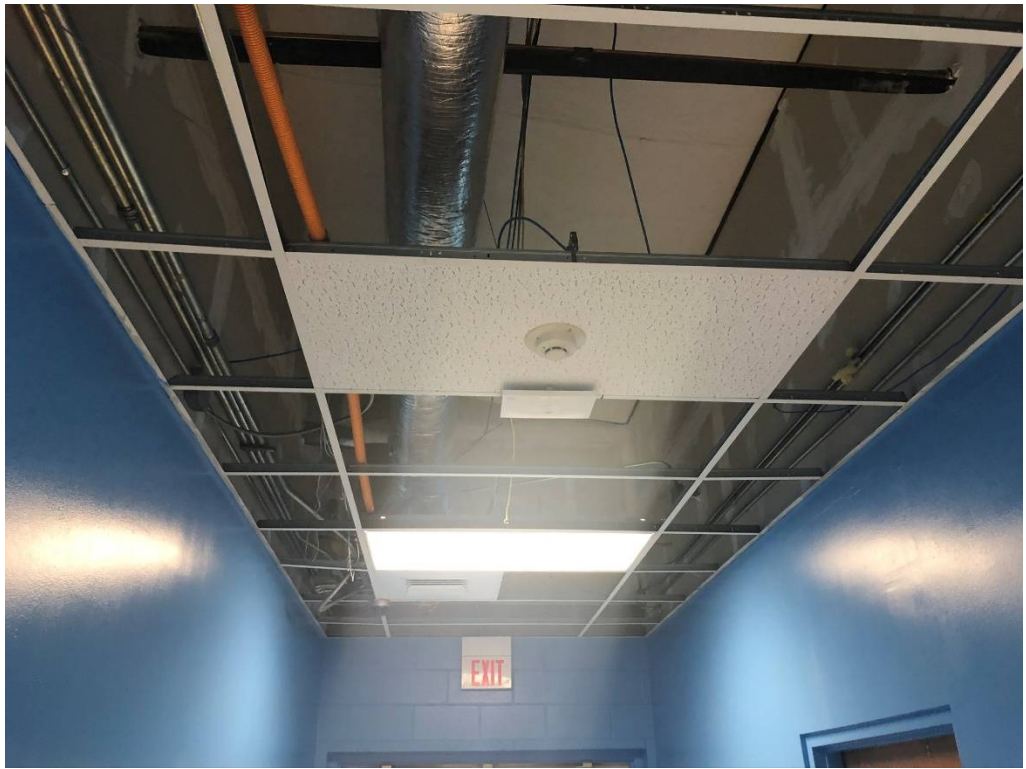


Figure 1 – Ceiling Tiles Removed in Hall



Figure 2 – Ceiling Tiles Removed in Hall

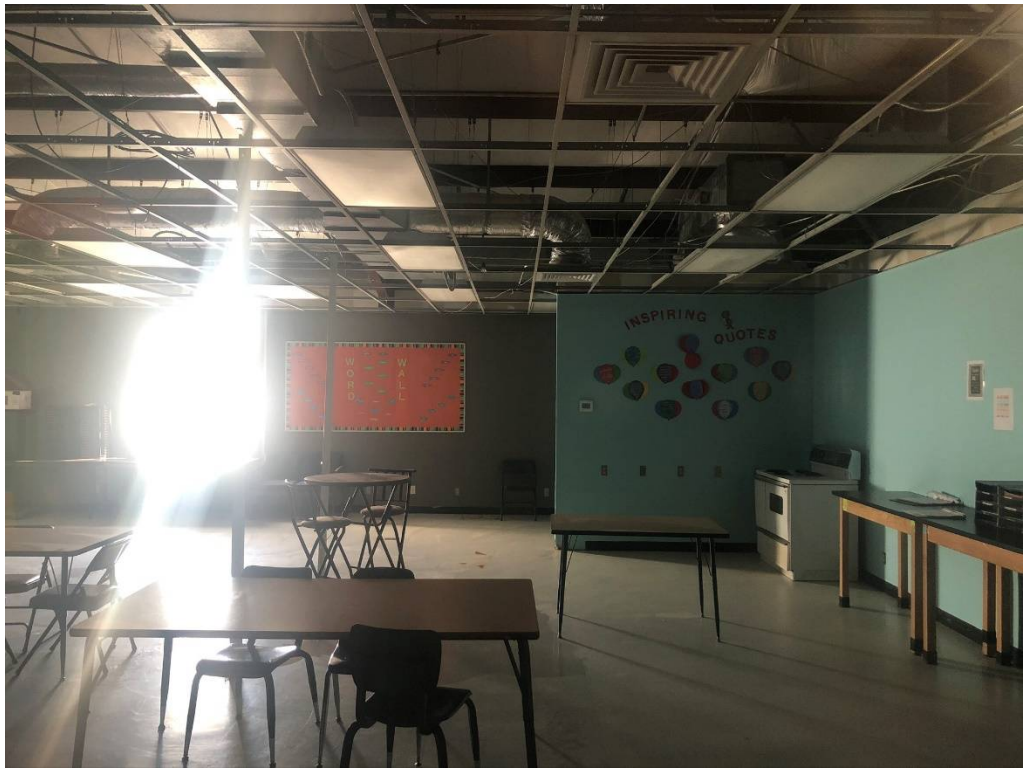


Figure 3 – Ceiling Tiles Removed in Classrooms



Figure 4 – Ceiling Tiles Removed in Classrooms



Figure 5 – Debris Trail (sidewalk to be replaced)



Figure 6 – Formwork and Rebar on Site



Figure 7 – Ceiling Tiles Removed in Main Hall



Figure 8 – Ceiling Tiles Removed



Figure 9 – Storage Room E-102C



Figure 10 – Lights Suspended after Demo of Grid
