

## Architect's Field Report

201 Park Court, Suite B  
Ridgeland, MS 39157  
P 601.790.9432  
F 888.281.0547

22 May 2020

18059-AOI Academy of Innovation / Report Number 036

One Jackson Place, Suite 250  
188 East Capitol Street  
Jackson, MS 39201-2100  
P 601.352.5411  
F 601.352.5362

Contract Century Construction  
Date / Time 21 May 2020 / 4:30 AM  
Weather / Temp Clear / 86 ° F  
Est % Complete 58%  
Sched Conformance + 68 days  
Work in Progress Exterior Framing  
Exterior Sheathing

161 Lameuse Street, Suite 201  
Biloxi, MS 39530  
P 228.374.1409  
F 228.374.1414

Present at Site Billy Burwell, Century Construction  
Paul Purser, DBA

Observations I arrived onsite and entered from the North Entrance. Exterior Framing was in progress here. I walked the site in a counter clockwise pattern at the exterior. Gas Pipe progress has been made and is being tested at the lower level.

At the south courtyard, sheathing progress was ongoing. I noted some damage to exterior sheathing. I spoke with Billy Burwell, CC, about this and he mentioned that there were 3 spots to his knowledge that were damaged by an installer but that they would be repaired soon. He also mentioned that storefront should be here soon and that roofers should be working on completing the install next week.

After walking the interior, it appears that light gauge framing is still in progress but that most of the interior walls are in place and only furr-downs and ceiling work remain.

Items to Verify None

Action Required None

Report By:

Paul Purser, AIA, LEED AP  
Dale | Bailey, an Association

cc: Wilson Little / Joey Moore / Allison Wood (CC)  
Chad Shealy / Shaquita Burke / Christi Kilroy (VWSD)  
Gary Bailey / Jason Stewart / Mark Pipper (BPM)  
Russ Blount / Will Commarato / Candy Failor (DBA)  
Brandon McKay / Austin Newell (WGK)  
Jason Kackley / Al Guynes (GSK)  
Chris Green / Larry Scott (TPS)  
Jerry Montgomery (SM)



Figure 1 – North Structure Framing Ongoing



Figure 2 – Drop Off Awning Red Steel Partially Complete



Figure 3 – Road and Parking Graded and Ready for Substrate



Figure 4 –West Elevation of North Structure



Figure 5 – West Structure Sheathing and Water Proofing Ongoing



Figure 6 – Gas Pipe Installed at Kitchen



Figure 7 – Gas Pressure Test in Progress



Figure 8 – South Façade Framing and Sheathing Ongoing



Figure 9 – South Courtyard Sheathing in Progress



Figure 10 – Some Damage to be Repaired at Sheathing on South Façade



Figure 11 – Interior Framing Ongoing

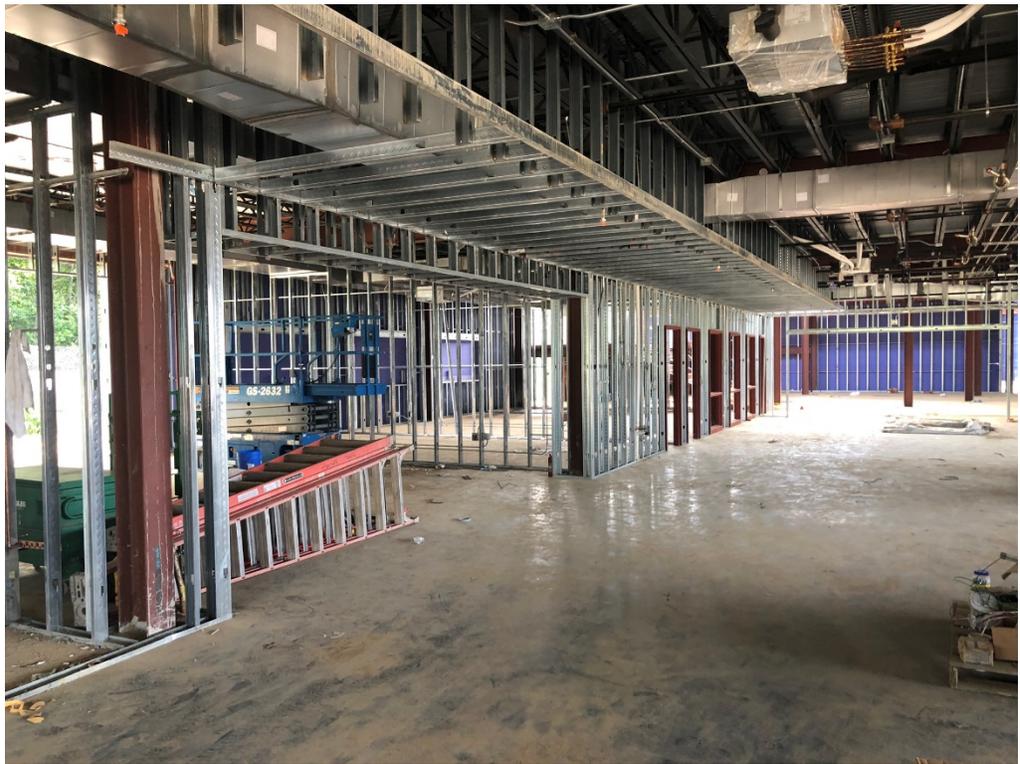


Figure 12 –Interior Framing Ongoing

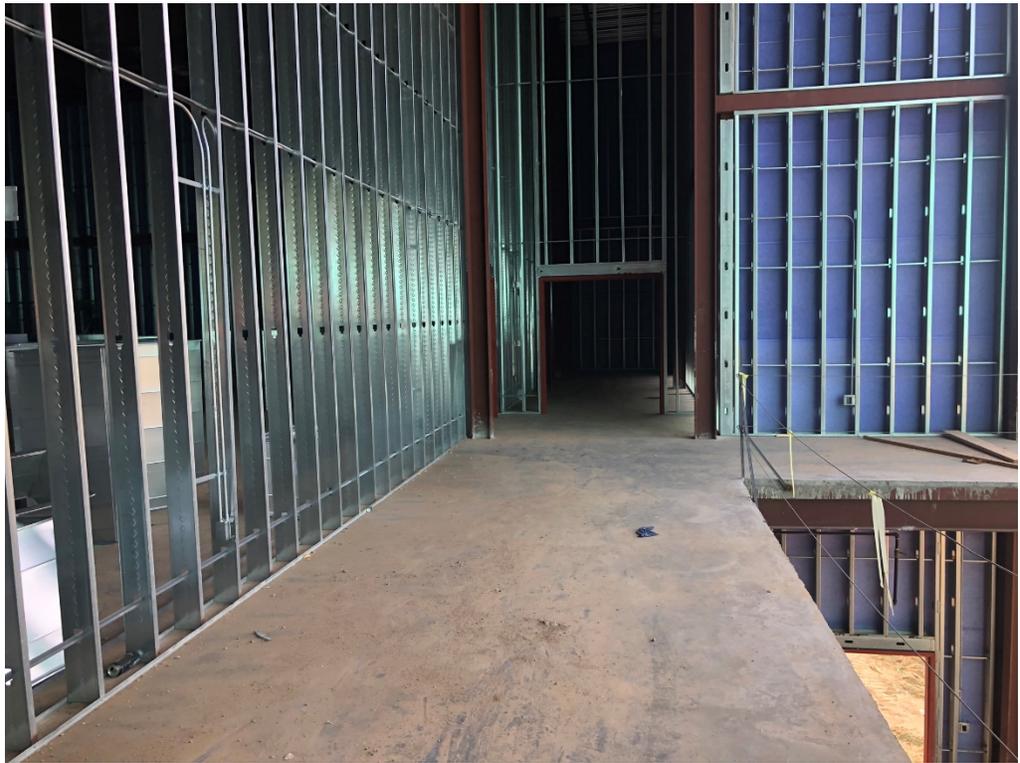


Figure 13 – Interior Framing Ongoing



Figure 14 – Duct Installation at Gym in Progress
