

Architect's Field Report

201 Park Court, Suite B
Ridgeland, MS 39157
P 601.790.9432
F 888.281.0547

17 October 2020

18059-AOI Academy of Innovation / Report Number 047

One Jackson Place, Suite 250
188 East Capitol Street
Jackson, MS 39201-2100
P 601.352.5411
F 601.352.5362

Contract Century Construction

Date / Time 14 October 2020 / 10:30 AM

Weather / Temp Clear / 76 ° F

Est % Complete 60%

Sched Conformance + 68 days

Work in Progress Mechanical Installation
Drywall Finishing
Grid Installation
Tile Floor and Wall Installations
Glazing Install

161 Lameuse Street, Suite 201
Biloxi, MS 39530
P 228.374.1409
F 228.374.1414

Present at Site Joey Moore, CC
Paul Purser, DBA

Observations Arriving on site, I walked the exterior of the building from north to east to south to west. Glazing installers were on site at storefront installations. Some work was also being performed on the central entry glass curtain wall.

Inside, drywallers were finishing panels. Tile Installers were cleaning up tile and getting ready for grout. Electrical service workers were pulling wire. Welders were grinding and cleaning up steel rails.

Items to Verify None

Action Required None.

Report By:

Paul Purser, AIA, LEED AP
Dale | Bailey, an Association

cc: Wilson Little / Joey Moore / Allison Wood (CC)
Chad Shealy / Shaquita Burke / Christi Kilroy (VWSD)
Gary Bailey / Jason Stewart / Mark Pipper (BPM)
Russ Blount / Will Commarato / Candy Failor (DBA)
Brandon McKay / Austin Newell (WGK)
Jason Kackley / Al Guynes (GSK)
Chris Green / Larry Scott (TPS)
Jerry Montgomery (SM)

dalepartners.com

baileyarch.com

Architects Who Know Education



Figure 1 – North Central Façade of Structure (Glazing Install)



Figure 2 – Progress at Car Drop Off



Figure 3 – Framed Plinths



Figure 4 – Framed Plinths



Figure 5 – NE Looking SW



Figure 6 – East Section of Building Exterior



Figure 7 – East Façade



Figure 8 – East Façade



Figure 9 – South Façade



Figure 10 – South Façade



Figure 11 – South Façade



Figure 12 – South Façade



Figure 13 – Courtyard



Figure 14 – Courtyard



Figure 15 – Drywall Finishing is Ongoing



Figure 16 – Tile is Ongoing



Figure 17 – Tile is Ongoing

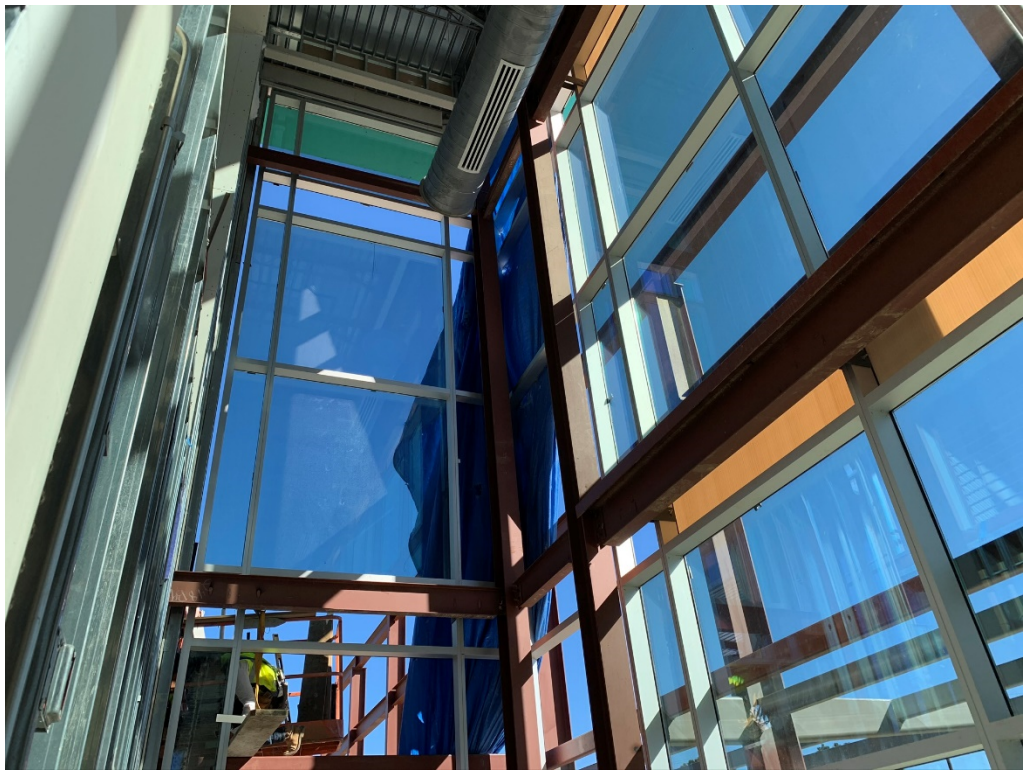


Figure 18 – Entry 2 Story Space



Figure 19 – Entry 2 Story Space



Figure 20 – Entry 2 Story Space



Figure 21 – East Building 2nd Floor



Figure 22 – East Building 3rd Floor



Figure 23 – Central Upper Lobby



Figure 24 – Upstairs Bathroom Tile is nearing Completion



Figure 25 – Upstairs Lobby Looking West



Figure 26 – Upstairs Lobby Looking North



Figure 27 – Upstairs Bathroom Tile is nearing Completion; Ceiling Grid is Installed where Wall Finishes are Complete



Figure 28 – Ceiling Grid is Installed where Wall Finishes are Complete



Figure 29 – Steel Handrail Progress



Figure 30 – Grinding Work at Steel Rail



Figure 31 – Electrical Wire Pull



Figure 32 – Exterior Southwest Stair Installed
