

Architect's Field Report

201 Park Court, Suite B

Ridgeland, MS 39157

28 March 2022

Observations

P 601.790.9432

F 888.281.0547

21064 Pontotoc City Schools ESSR / Report Number 001

One Jackson Place. Suite 250

188 East Capitol Street Date / Time

Jackson, MS 39201-2100

P 601.352.5411

F 601.352.5362

Contract Flagstar Construction, Inc.

21 March 2022 / 10:00 AM

Weather / Temp Partly cloudy / 67 ° F

Present at Site Mike Parker, Flagstar

Zeb Collums, Flagstar Dr. Michelle Bivens, PCS Wally Windham, PCS

161 Lameuse Street, Suite 201

Biloxi, MS 39530

P 228.374.1409

F 228.374.1414

I arrived on site prior to our monthly OAC meeting to walk the site. Work

is progressing nicely. I am concerned that block has not started in the High School but have been told that it is forthcoming. Materials for that

work are staged and ready to go.

Paul Purser, Dale Partners Architects

Demo has been performed throughout including Asbestos Abatement. Ceilings have been removed everywhere except for the HS toilet room which is not slated for work until the summer. Excavation is underway

at the Junior High and moving along according to schedule.

After our meeting, we walked the site. 2 items of work are under review and need further discussion prior to continuation: the ADA ramp at the

Middle School & the Ceiling and lighting work at the Junior High.

Items to Verify None.

Action Required None.

Report By: Paul Purser

Paul Purser
AIA, Architect, Dale Bailey, An Association

cc: Dr. Michelle Bivens, Pontotoc City Schools

Wally Windham, Pontotoc City Schools Gary Bailey, Dale Bailey, An Association Russ Blount, AIA, Dale Bailey, An Association Luigia Hodge, Dale Bailey, An Association

dalepartners.com

baileyarch.com

Architects Who Know Education



Figure 1 – HS Interior Progress; ready for new walls



Figure 2 – Block @ HS



Figure 3 – Mortar & Sand



Figure 4 – Construction Dumpster Location



Figure 5 – HS Sidewalk Demo



Figure 6 – HS Door Opening Demo

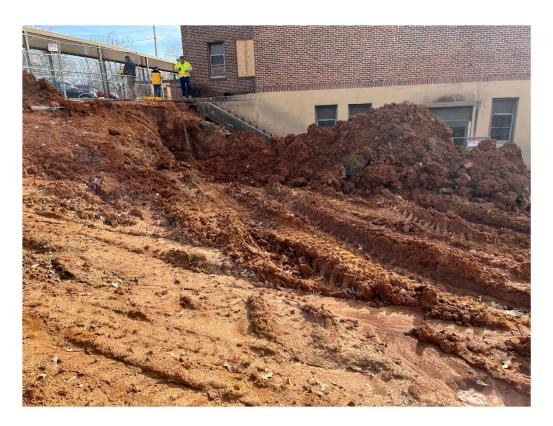


Figure 7 – Excavation @ JH Ramp

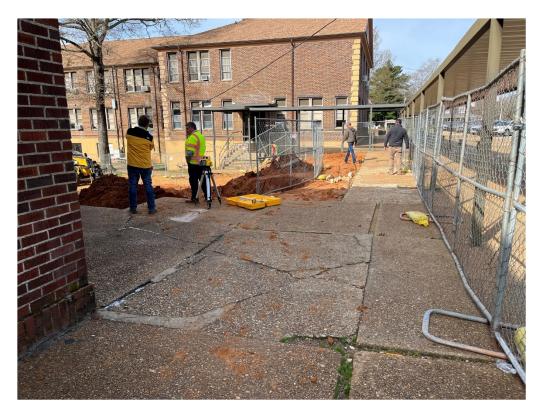


Figure 8 – JH Ramp Progress from Above



Figure 9 – Protective Site Barriers in Place



Figure 10 – Excavation @ JH Ramp



Figure 11 – Site Protective Barriers



Figure 12 – Demo @ Middle School



Figure 13 – Demo @ Middle School



Figure 14 – Demo @ Middle School



Figure 15 – Demo @ Middle School



Figure 16 – Demo @ Middle School



Figure 17 – Demo @ Junior High



Figure 18 – Demo @ Junior High

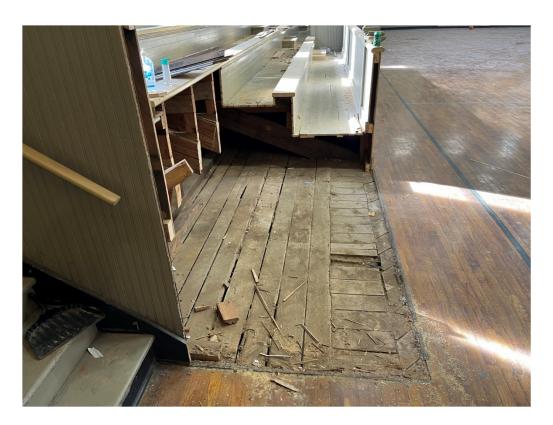


Figure 19 – Demo @ Junior High



Figure 20 – Demo @ Junior High



Figure 21 – Demo @ Junior High



Figure 22 – Demo @ Junior High



Figure 23 – Demo @ Junior High



Figure 24 – Demo @ Junior High

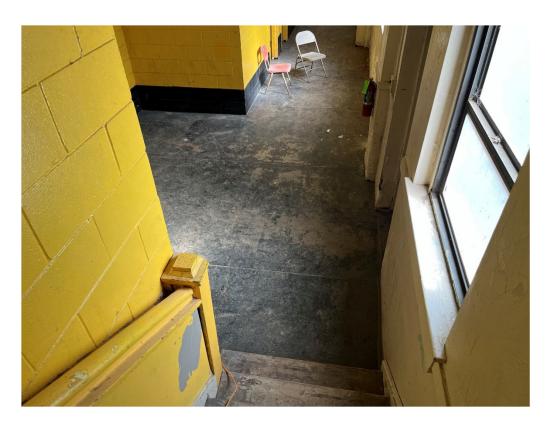


Figure 25 – Demo @ Junior High



Figure 26 – Demo @ Junior High



Figure 27 – Demo @ Junior High

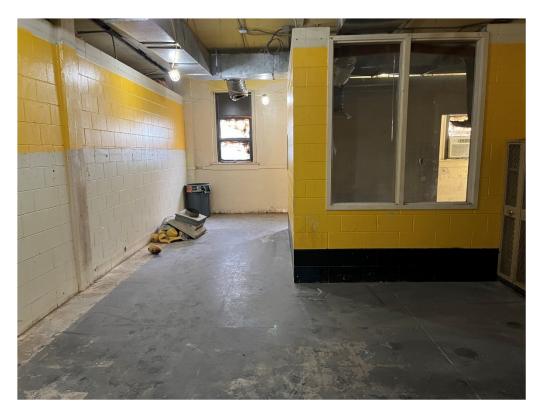


Figure 28 – Demo @ Junior High
