

12 January 2023

21097 Greenwood Leflore Consolidated SD ESSER / Report Number 001

201 Park Court, Suite B Ridgeland, MS 39157 P 601.790.9432 F 888.281.0547	Contract	Upchurch Plumbing, Inc.
	Date / Time	10 January 2023 / 2:00 PM
	Weather / Temp	Clear / 63 ° F
	Est % Complete	13%
One Jackson Place, Suite 250 188 East Capitol Street Jackson, MS 39201-2100 P 601.352.5411 F 601.352.5362	Sched Conformance	+/- 00 days
	Work in Progress	Fixture Install
	Present at Site	Upchurch Plumbing Paul Purser, DBA
161 Lameuse Street, Suite 201 Biloxi, MS 39530 P 228.374.1409 F 228.374.1414	Observations	<p>After our OAC meeting, I walked the schools where work has been performed. For the most part, Claudine Brown has been complete. Most things are in good order, but they do have some issues with leaking faucets and touchless sensors not working. Please review with the admin to determine what needs to be repaired.</p> <p>At Greenwood middle, work is ongoing. Urinal valves needed to be reordered due to a pipe size difference. Other work is nearing completion.</p> <p>At Amanda Elzy, plumbers were on site installing faucets. There was some additional work at this school I believe that was brought up with the owner. Please coordinate as you are able.</p> <p>There are a couple items that we would request pricing on and you can review these in the figures attached. If accepted, it is our recommendation to use contingency funds.</p>
	Items to Verify	None.
	Action Required	Provide pricing per Figures 3 & 8. Coordinate with Claudine Brown Admin on Repairs. Provide clarification on Figure 9.

Report By:



paul purser, Architect
Dale | Bailey, an Association

cc: Brad Hawkins / Craig Bontrager / Scott Upchurch (Upchurch)
James Johnson-Waldington / Torien Howard / Cynthia House (GLCSD)
Gary Bailey / Jason Stewart / Mark Pippet (BPM)
Russ Blount / Sabrena Patrick (DBA)
Jason Kackley / Al Guynes (GSK)



Figure 1 - Typical Finished Installation at Claudine Brown



Figure 2 – Typical Urinal Valves



Figure 3 – Please Provide Price to replace sink on right with like sink as on left



Figure 4 – Typical New Faucet @ Claudine Brown



Figure 5 – Typical New Faucet @ Claudine Brown



Figure 6 – This Faucet Does not Appear to respond at Claudine Brown



Figure 7 – Some Faucets Dripping @ Claudine Brown

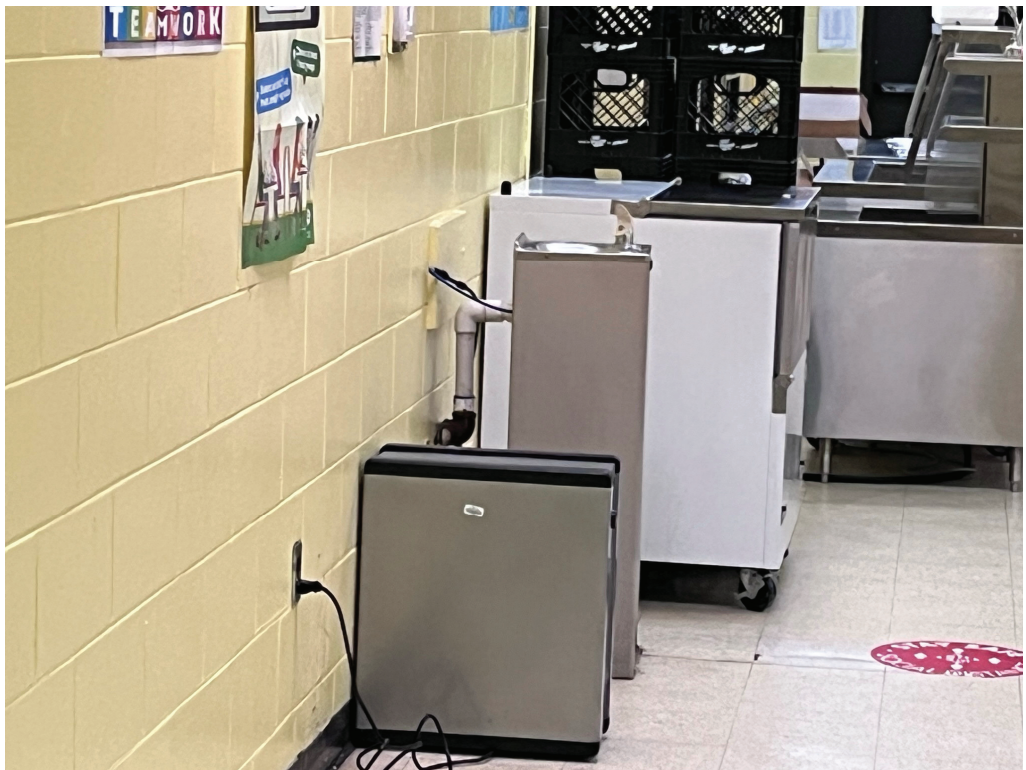


Figure 8 – Please Provide Price to Install Partial Height Wall and Bottle Filler Here in Cafeteria at Claudine Brown



Figure 9 – 2 New Bottle Fillers in Plans for here; is the other still to come?



Figure 10 – Typical New Faucet @ Greenwood Middle



Figure 11 – Typical New Faucet @ Greenwood Middle



Figure 12 – Typical New Flush Valve @ Greenwood Middle



Figure 13 – Upchurch On Site at Amanda Elzy



Figure 14 – New Faucets at Amanda Elzy
